WhatNext Vision Motors

Shaping the Future of Mobility with Innovation and Excellence

Project Planning and Scheduling - Project Planning

5.1 Project Planning

Overview

Project planning defines how the WhatNext Vision Motors Salesforce CRM is built, in what order, by whom and in what time. The project follows the Agile methodology, so work is divided into small sprints, each delivering a working part of the vehicle order management system.

Planning Approach

Element	How it is used in the project
Agile methodology	Work is delivered in short, repeated cycles so that progress can be reviewed and adjusted regularly.
Epics, Stories, Story Points	Each major feature area is an Epic. Epics are split into user stories, and each story is given story points to show its effort.
Sprint-based execution	Stories are grouped into sprints, and each sprint is assigned to team members with a priority.
Velocity calculation	Story points completed in a sprint are used to measure speed and to estimate future sprints.

Planning Hierarchy

Functional requirement area — *As a user, I want ... so that ...* — *Effort estimate*

Product Backlog and Sprint Schedule

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Member
Sprint-1	Developer Setup	USN-1	As a system administrator, I want to create and configure a Salesforce developer account so that I can build and deploy the vehicle order management system.	3	High	Member1

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Member
Sprint-2	Data Modeling	USN-2	As an admin, I want to create Vehicle, Dealer, Customer, Order, and Service Request objects with proper relationships so that all business data is stored and managed systematically.	5	High	Member2
Sprint-2	Data Modeling	USN-3	As a staff member, I want dedicated tabs and a Lightning App for all modules so that I can easily navigate and manage vehicle orders and dealer operations.	5	High	Member3
Sprint-3	Automation	USN-4	As a system, I want to validate stock availability, mandatory fields, and order inputs so that invalid or incomplete vehicle orders are prevented.	3	High	Member4
Sprint-3	Automation	USN-5	As a sales coordinator, I want automated flows to assign the nearest dealer and update order status so that processing becomes faster and requires minimal manual effort.	3	High	Member4
Sprint-4	Apex	USN-6	As a system, I want Apex triggers to automatically perform actions such as order confirmation and dealer assignment so that critical processes occur instantly and accurately.	5	High	Member1
Sprint-4	Apex	USN-7	As an inventory manager, I want batch jobs to update vehicle stock levels automatically so that inventory data remains accurate and up to date.	5	High	Member2
Sprint-5	Reports	USN-8	As a manager, I want reports showing order status, dealer performance, and sales metrics so that I can monitor operations and make informed decisions.	4	High	Member3
Sprint-6	Dashboards	USN-9	As a manager, I want dashboards showing order status, dealer performance, and sales metrics so that I can monitor operations and make informed decisions.	4	Medium	Member4

Project Tracker

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	20	6 Days	24 Oct 2022	29 Oct 2022	20	29 Oct 2022
Sprint-2	20	6 Days	31 Oct 2022	05 Nov 2022	-	-
Sprint-3	20	6 Days	07 Nov 2022	12 Nov 2022	-	-
Sprint-4	20	6 Days	14 Nov 2022	19 Nov 2022	-	-

Velocity Calculation

Velocity shows how many story points the team completes in a sprint, and it is used to estimate how long the remaining work will take.

Measure	Calculation	Result
Sprint-1 velocity	Story points completed in the sprint	20 points
Sprint duration	Planned days in one sprint	6 days
Average velocity (per day)	20 story points / 6 days	**3.33 points per day**
Sprints needed (4 x 20 points)	Total points / velocity per sprint = 80 / 20	**4 sprints**

Burndown Chart

The burndown chart compares the planned (ideal) reduction of story points with the actual progress. Sprint-1 completed all 20 planned points on its release date, so the remaining work dropped from 80 to 60 points, exactly as planned.

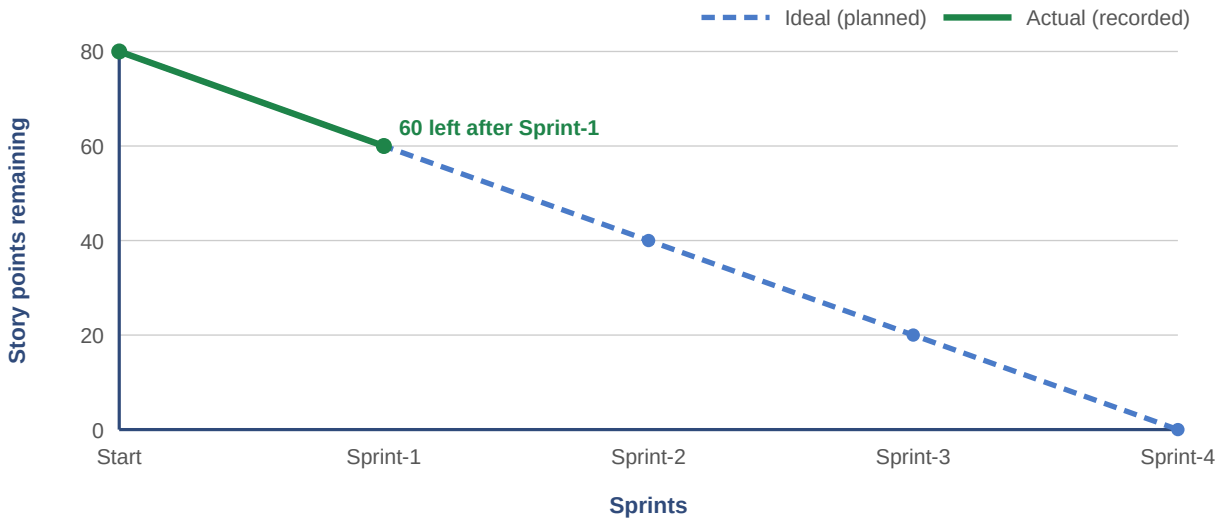

Conclusion

Agile planning with epics, stories, story points and sprints gives the team a clear order of work, shared responsibility and a measurable pace, which helps WhatNext Vision Motors deliver the CRM in a controlled and predictable way.
